

-ST-DMW149

馬鞍山診所側休憩公園加裝照明系統
Provision of lighting for the Leisure Park near Ma On Shan Health Centre



HAD – MINOR WORKS PROJECT – SHATIN DISTRICT 小型工程項目 - 沙田區

ARCHITECT/LEAD CONSULTANT

Tom Ip & Partners Architects Engineers & Development Consultants Limited

SUB - CONSULTANTS

Paul Wong Consulting Engineers Limited

Hyder Consulting Limited

Daniel Chan & Associates Limited

Landscape Architectural Earthasis Limited

QUANTITY SURVEYORS & CONTRACT MANAGEMENT CONSULTANTS

Rider Levett Bucknall

10 February 2011

1. 環境概況及建議項目內容
2. 項目預算
3. 項目工程時間表
4. 建造設計樣式

ST-DMW149

馬鞍山診所側休憩公園加裝照明系統


環境概況及 建議項目

馬鞍山診所側休憩公園，為方便居民及長者，
需加裝照明系統約 3.5米高及更換標誌牌。


於下圖位置



環境概況

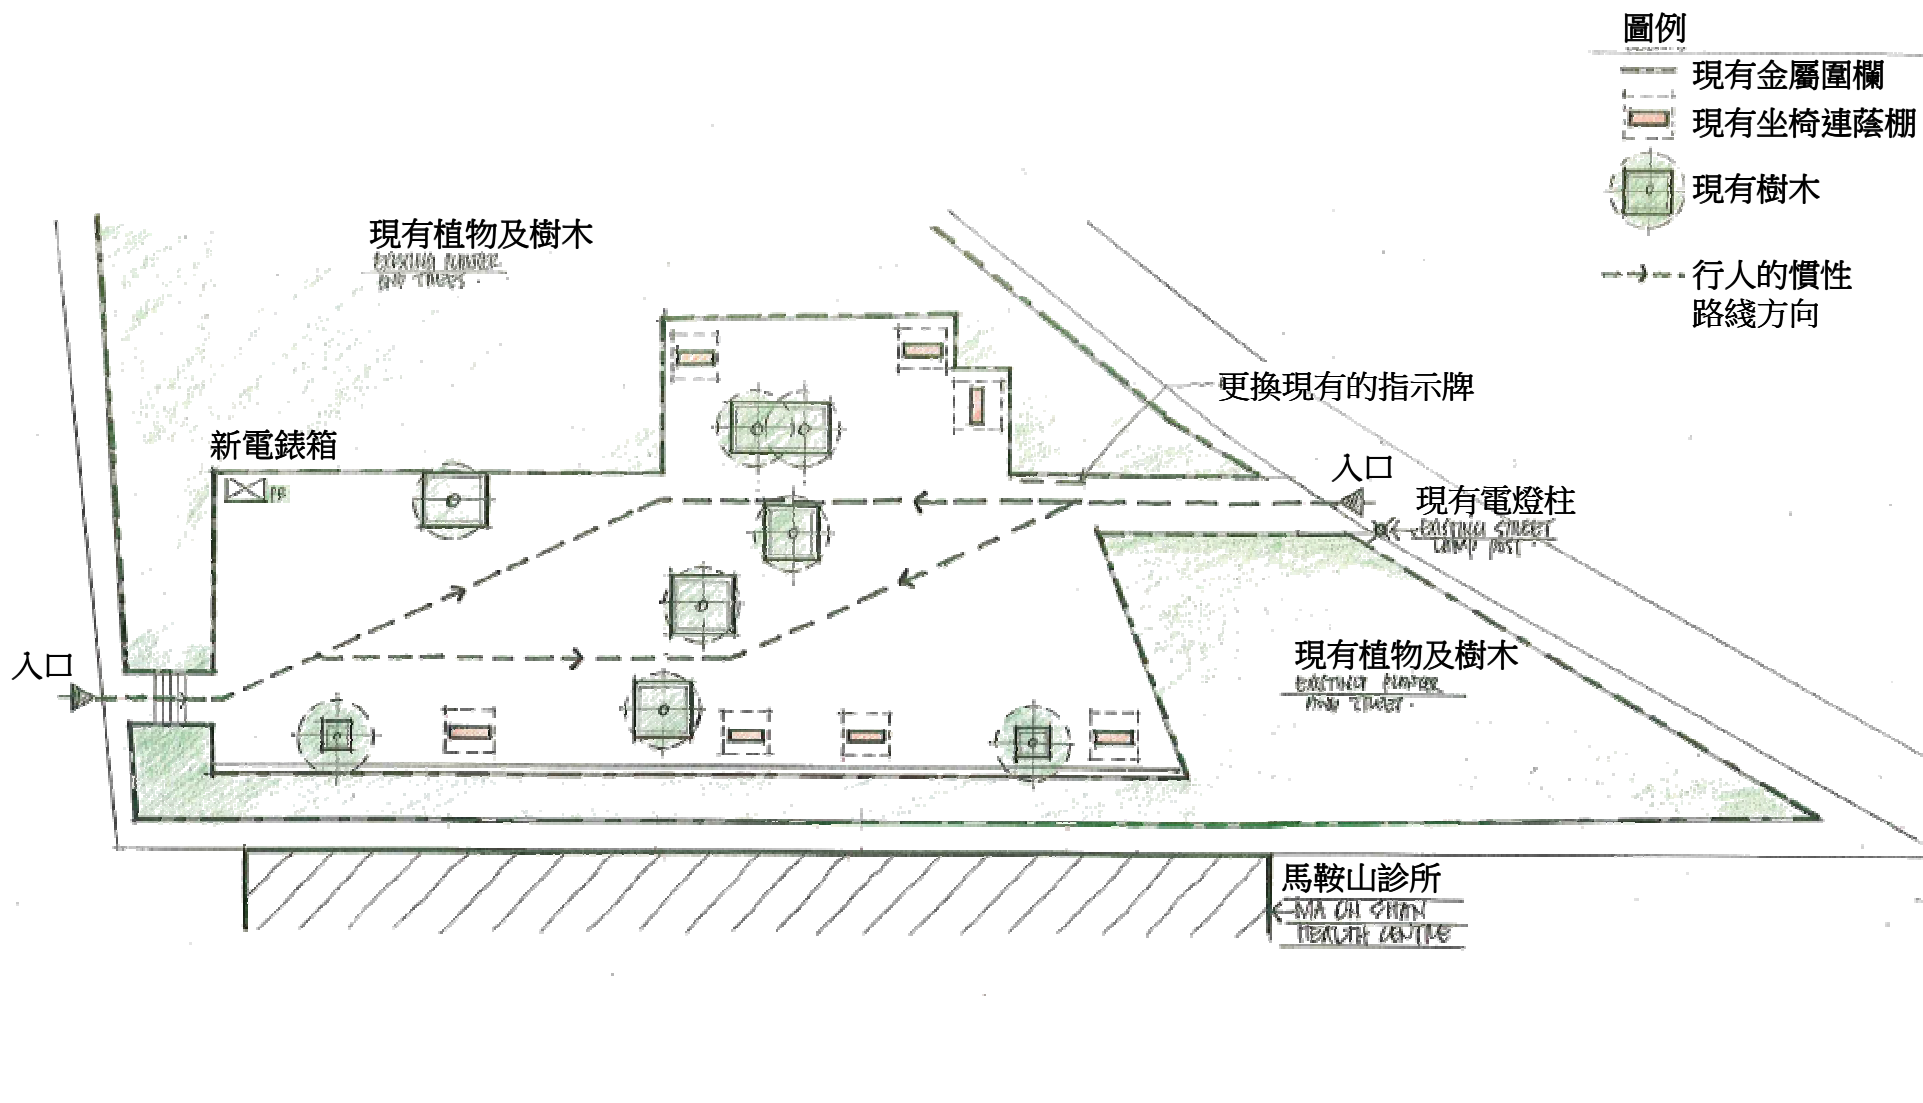

項目方案

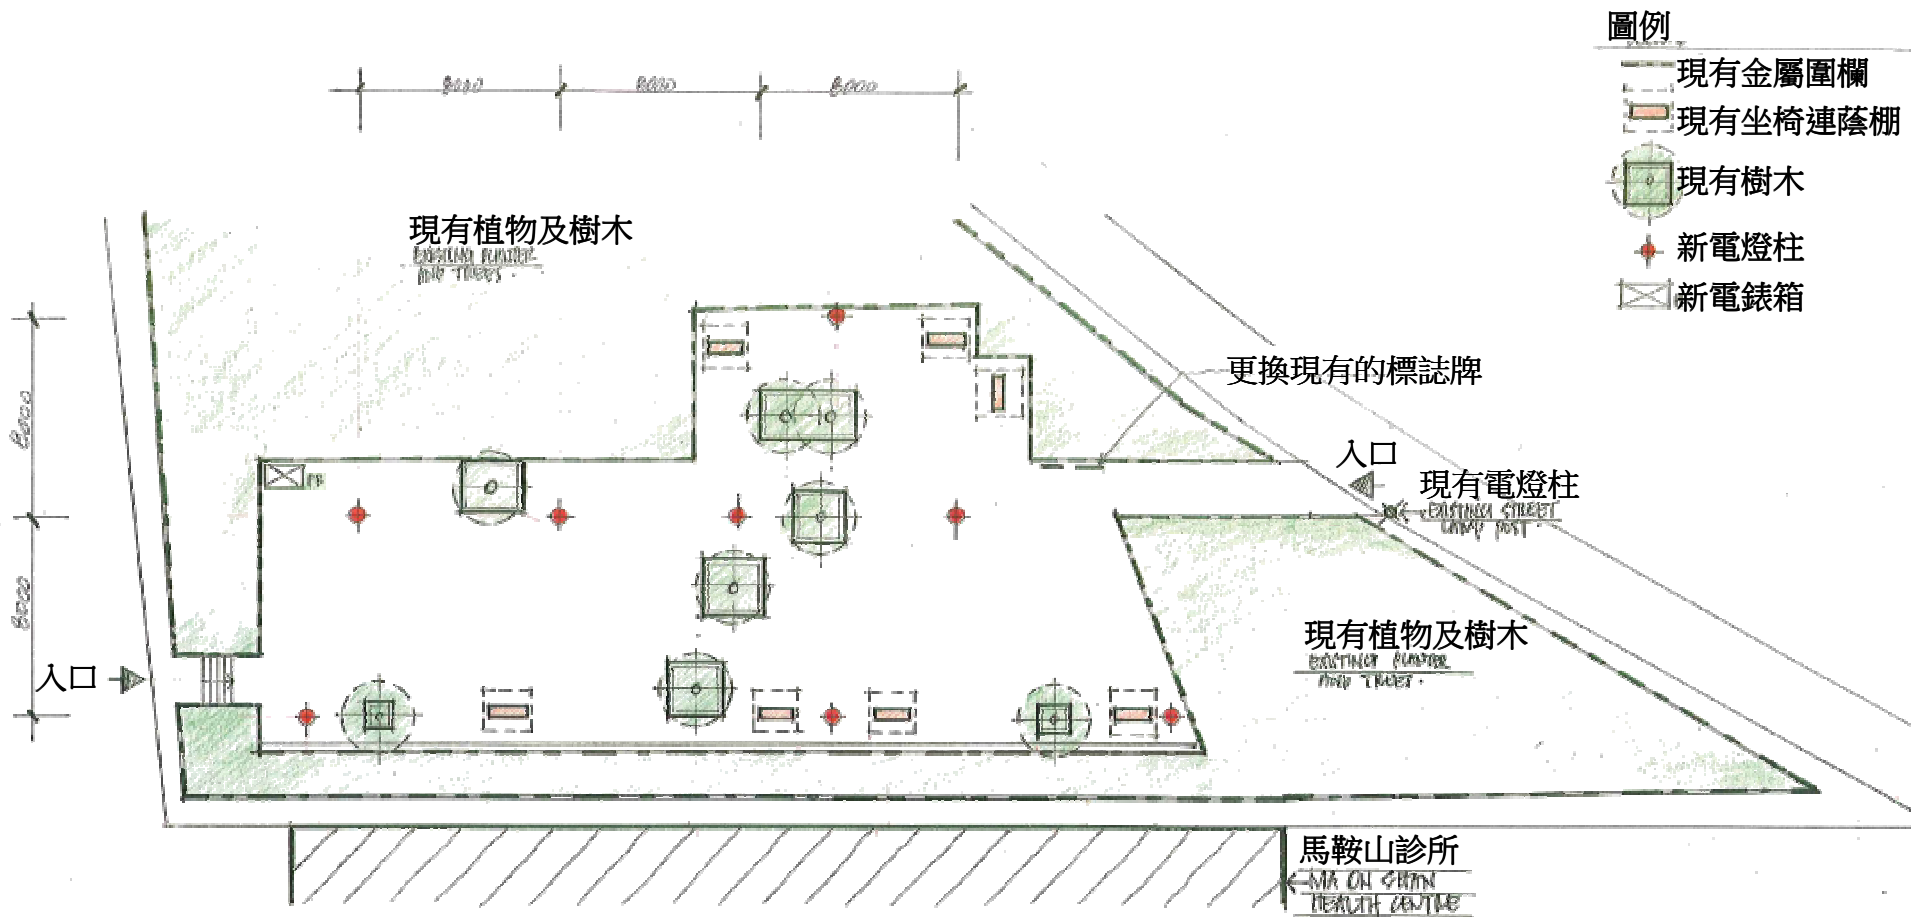

ST-DMW149

馬鞍山診所側休憩公園加裝照明系統

電燈柱樣式



*圖片只供參考

項目預算

ST-DMW149

馬鞍山診所側休憩公園加裝照明系統

工程編號： ST-DMW149

工程名稱： Provision of Lighting for the Leisure Park near Ma On Shan Health Centre

粗略工程預算

預算費用

(1) 粗略建築費用估價	759,000
(2) 其他工程費用	
(2.1) 顧問費用	156,000 **
(2.2) 駐地盤工程監督費用	66,000

總數： **981,000**

** 實際顧問費用以投標價為準

項目預算

ST-DMW149

馬鞍山診所側休憩公園加裝照明系統

工程編號：**ST-DMW149**

工程名稱：**Provision of Lighting for the Leisure Park near Ma On Shan Health Centre**

工程現金流預算

<u>財政年度</u>	<u>該年度現金流</u>	<u>累計現金流</u>
2011/12	\$176,000	\$176,000
2012/13	\$719,000	\$895,000
2013/14	\$86,000	\$981,000













項目工程時間表

HAD Minor Works - ST-DMW- 149 Provision of Lighting for the Leisure Park near Ma On Shan Health Centre

ID	Task Name	Duration	Start	Finish	2011				2012				2013				
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1				
1	可行性研究 Feasibility Study	2 mons	Mon 10/1/11	Thu 3/3/11													
2	初步設計與詳細設計 Schematic Design and Detail Design	3 mons	Fri 4/3/11	Fri 3/6/11													
3	文件與投標 Documentation and Tendering	4 mons	Sat 4/6/11	Mon 3/10/11													
4	準備文件 Documentation	1.5 mons	Sat 4/6/11	Mon 18/7/11													
5	完成投標 Tendering and Award	2.5 mons	Tue 19/7/11	Mon 3/10/11													
6	建造施工 Construction	5 mons	Tue 4/10/11	Sat 3/3/12													
7	完成全部工程 DLP	12 mons	Sun 4/3/12	Sun 3/3/13													

 雨水期 Inclement Weather (2 mons)

Programme
Date: 19 August 2010
Prepared by: CH

Task		Rolled Up Task		External Tasks	
Progress		Rolled Up Milestone		Project Summary	
Milestone		Rolled Up Progress		Group By Summary	
Summary		Split		Deadline	

Note:
1. All days in Duration column are counted as calendar days

■ END
