

「中環灣仔繞道和東區走廊連接路（中環灣仔繞道）」工程項目

工程進度簡報(2011 年 5 月 26 日)

1. 引言

在 2011 年 1 月 27 日舉行的中西區區議會交通及運輸委員會會議上，委員會要求路政署在往後的會議上匯報中西區內中環灣仔繞道工程的最新進展及即將開展的工程摘要。

2 中環灣仔繞道工程進度(2011 年 3 月至 2011 年 5 月)：

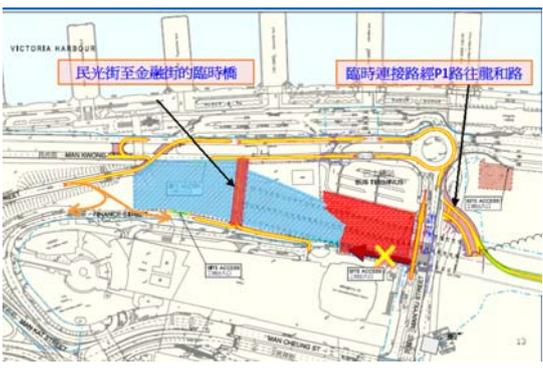
位置	工序	圖片
國際金融中心二期對出的草地	(1) 地下公共設施遷移工程	 <p>04/04/2011 10:17</p> <p>地下公共設施遷移工程</p>
	(2) 隧道隔牆的前期工程-(試驗坑挖掘)	 <p>隧道隔牆的前期工程-(試驗坑挖掘)</p>

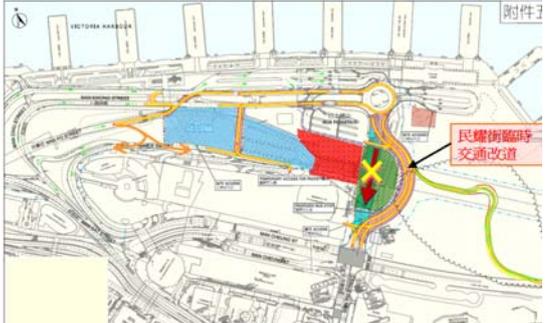
<p>民寶街， 民光街及 金融街</p>	<p>臨時交通改道 - 民寶街至民光街的臨時交通改道及民寶街至金融街的臨時連接路</p>	 <p>改道後民寶街及民光街交通路口</p> <p>民寶街至金融街的臨時連接路</p>
------------------------------	--	---

3. 中環灣仔繞道工程未來六個月進行的工程(2011 年 6 月至 2011 年 11 月)：

位置	工序	圖片
金融街	地底渠務設施改道工程	
國際金融中心二期對出的草地	隧道挖掘工程	

3. 中環灣仔繞道工程未來一年內之臨時交通安排(2011 年 6 月至 2012 年 5 月)：

預計實施時間	臨時交通安排	圖片
2011 年底	由民光街西行通往金融街的臨時橋	
2012 年初	由民耀街迴旋處經 P1 路往龍和路的臨時連接路	

<p>2012 年中</p>	<p>民耀街臨時交通改道</p>	 <p>The map illustrates the temporary traffic diversion for Min Yau Street in 2012. It shows the street layout around the Victoria Harbour waterfront, with various streets and landmarks labeled. A red area indicates the closed section of Min Yau Street, and a yellow 'X' marks the diversion point. A red box with a black arrow points to the diversion route, labeled '民耀街臨時交通改道'. The map also includes a north arrow and the text '附件 2' in the top right corner.</p>
----------------	------------------	---
