

Tuen Mun District Council
2024-2027 District Facilities and Works Committee

Progress Report on Other Government Departments' Works Projects (as at 31.8.2024)

No.	Items	Government Departments	Progress Reports
A.	Drainage Services Department's Progress Report	Drainage Services Department	See Annex I
B.	Progress Report of Water Main Laying Works in Tuen Mun District by the Water Supplies Department	Water Supplies Department	See Annex II *

* Only Chinese version is available

Drainage Services Department's Progress Report

I. Progress of Recent Channel Desilting at Tuen Mun River Channel (as at 31.08.2024)

Location	Length (m)	Department	(Anticipated Commencement Date) Actual Commencement Date	(Anticipated Completion Date) Actual Completion Date	Progress/Remarks
Pui To Road to Tuen Ma Line Siu Hong Station	2400	DSD	04/2024	06/2024	Works completed
			07/2024	(09/2024)	Works in progress
			(10/2024)	(12/2024)	Works under planning
Tuen Yee Street to Yau Oi Bridge	640	CEDD	09/2019	03/2020	Works completed

II. Dredging Works at Wholesale Fish Market in Area 44 and Tuen Mun Typhoon Shelter

CEDD completed the dredging works at Tuen Mun Typhoon Shelter Phase 1 and Phase 2 in end April 2020 and end April 2021 respectively. The locations are shown in Figure 1.

III. Tuen Mun Village Sewerage

Contract No. DC/2020/07 – Village Sewerage in Northern Tuen Mun

The project includes the construction of one sewage pumping station at Fuk Hang Tsuen (Lower) and related village sewerage systems in Siu Hang Tsuen, Po Tang Ha, Tsz Tin Tsuen, Fuk Hang Tsuen (Lower). The contract commenced in January 2021 and was anticipated to be substantially completed in 2024 Q4.

Drainage Services Department

August 2024

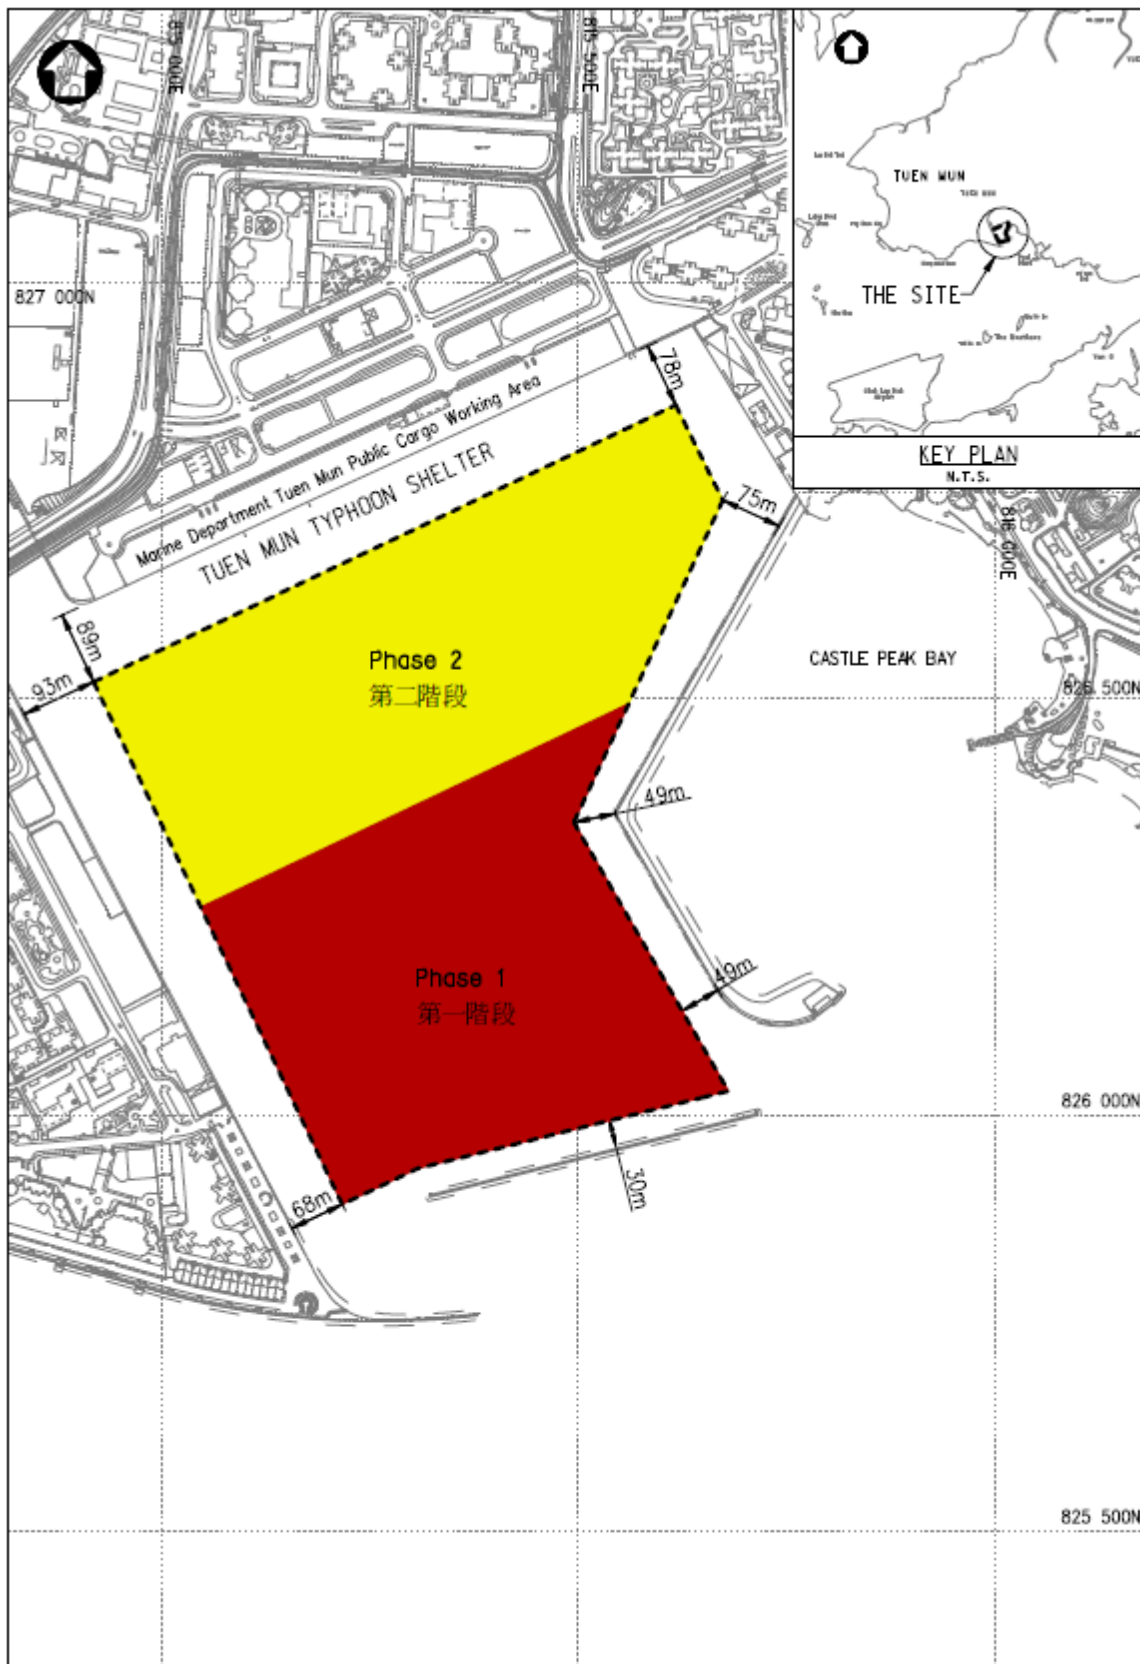


Figure 1: Location Plan of Tuen Mun Typhoon Shelter Dredging Works

水務署有關屯門區水管修復或敷設工程的進度匯報 (截至 8 月 31 日)

為改善屯門區內供水設施，水務署現正在區內進行的水管工程合約如下：

進行之水管修復或敷設工程及進度如下：

編號	合約編號	工程位置	長度 (米)	水管直徑 (毫米)	動工日期	完工日期	進度	備註
1	12/WSD/20	青賢街、河旁街、屯門鄉事會路	540	40 100	Q2/2022	Q4/2024	85%	鋪設水管進行中。
2	12/WSD/20	屯富路	240	50	Q2/2022	Q2/2024	100%	鋪設水管完成。
3	12/WSD/20	屯貴路	130	50	Q4/2021	Q2/2024	100%	鋪設水管完成。
4	12/WSD/20	龍鼓灘	2000	25 40 80	Q4/2022	Q2/2024	100%	鋪設水管完成。
5	12/WSD/20	華發街	600	150 200	Q3/2023	Q4/2024	50%	鋪設水管進行中
6	3/WSD/21	湖山路至湖翠路	1440	200 250	Q3/2022	Q4/2024	85%	鋪設水管進行中。
7	3/WSD/21	屯門公園近愛德里及愛明里	1040	600	Q1/2023	Q4/2024	90%	鋪設水管進行中。
8	3/WSD/21	澤豐街	72	80	Q3/2023	Q2/2024	100%	鋪設水管完成。
9	3/WSD/21	康輝路	120	375	Q2/2023	Q3/2024	100%	鋪設水管完成。
10	3/WSD/21	龍門路	200	900	Q4/2023	Q4/2024	15%	鋪設水管進行中。
11	3/WSD/21	屯門鄉事會路 近屯興路	80	375	Q1/2024	Q1/2025	40%	鋪設水管進行中。
12	12/WSD/20	天后路	20	150	Q2/2022	Q4/2024	85%	鋪設水管進行中。

計劃中的水管修復或敷設工程如下：

合約編號	工程位置	長度 (米)	水管直徑 (毫米)	動工日期	完工日期	備註
3/WSD/21	屯門鄉事會路 近友愛邨	150	375	Q3/2024	Q1/2025	此路段工程將會於通過試路後隨即展開。
3/WSD/21	杯渡路	290	200 400	Q3/2024	Q4/2024	路政署掘路許可證申請中。
3/WSD/21	屯門石排頭路	195	50	Q3/2024	Q2/2025	由於地下管線密集，臨時交通

	近建發街		100			安排正在作出調整。路政署掘路許可證申請中。
			150			
			250			

水務署
2024 年 8 月
