

**Tuen Mun District Council**  
**2024-2027 District Facilities and Works Committee**

**Progress Report on Other Government Departments' Works Projects (as at 28.2.2025)**

No.	Items	Government Departments	Progress Reports
A.	Drainage Services Department's Progress Report	Drainage Services Department	See <b>Annex I</b>
B.	Progress Report of Water Main Laying Works in Tuen Mun District by the Water Supplies Department	Water Supplies Department	See <b>Annex II</b> *

\* Only Chinese version is available

## Drainage Services Department's Progress Report

### I. Progress of Channel Desilting at Tuen Mun River Channel (as at 28.2.2025)

Location	Length (m)	Department	Actual Commencement Date (Anticipated Commencement Date)	Actual Completion Date (Anticipated Completion Date)	Progress/Remarks
Pui To Road to Tuen Ma Line Siu Hong Station	2400	DSD	10/2024	12/2024	Works completed
			01/2025	(03/2025)	Works in progress
			(04/2025)	(06/2025)	Works under planning
			(07/2025)	(09/2025)	Works under planning
Tuen Ma Line Tuen Mun Station to estuary	1800	CEDD	According to the bathymetric survey carried out in 2024 Q4, the riverbed level in the concerned river sections did not exceed the trigger level set by DSD. CEDD will continue to regularly carry out bathymetric survey and inspection to monitor the riverbed level. CEDD will carry out the dredging works if the riverbed level is found to affect the flood prevention capacity of Tuen Mun River.		

### II. Dredging Works at Wholesale Fish Market in Area 44 and Tuen Mun Typhoon Shelter

CEDD completed the dredging works for the Marine Department at Tuen Mun Typhoon Shelter Phase 1 and Phase 2 in end April 2020 and end April 2021 respectively. The locations are shown in **Figure 1**.


### III. Tuen Mun Village Sewerage

#### Contract No. DC/2020/07 – Village Sewerage in Northern Tuen Mun

The project includes the construction of one sewage pumping station at Fuk Hang Tsuen (Lower) and related village sewerage systems in Siu Hang Tsuen, Po Tang Ha, Tsz Tin Tsuen, Fuk Hang Tsuen (Lower). The contract commenced in January 2021 and is substantially completed in December 2024.

**Drainage Services Department**

**February 2025**

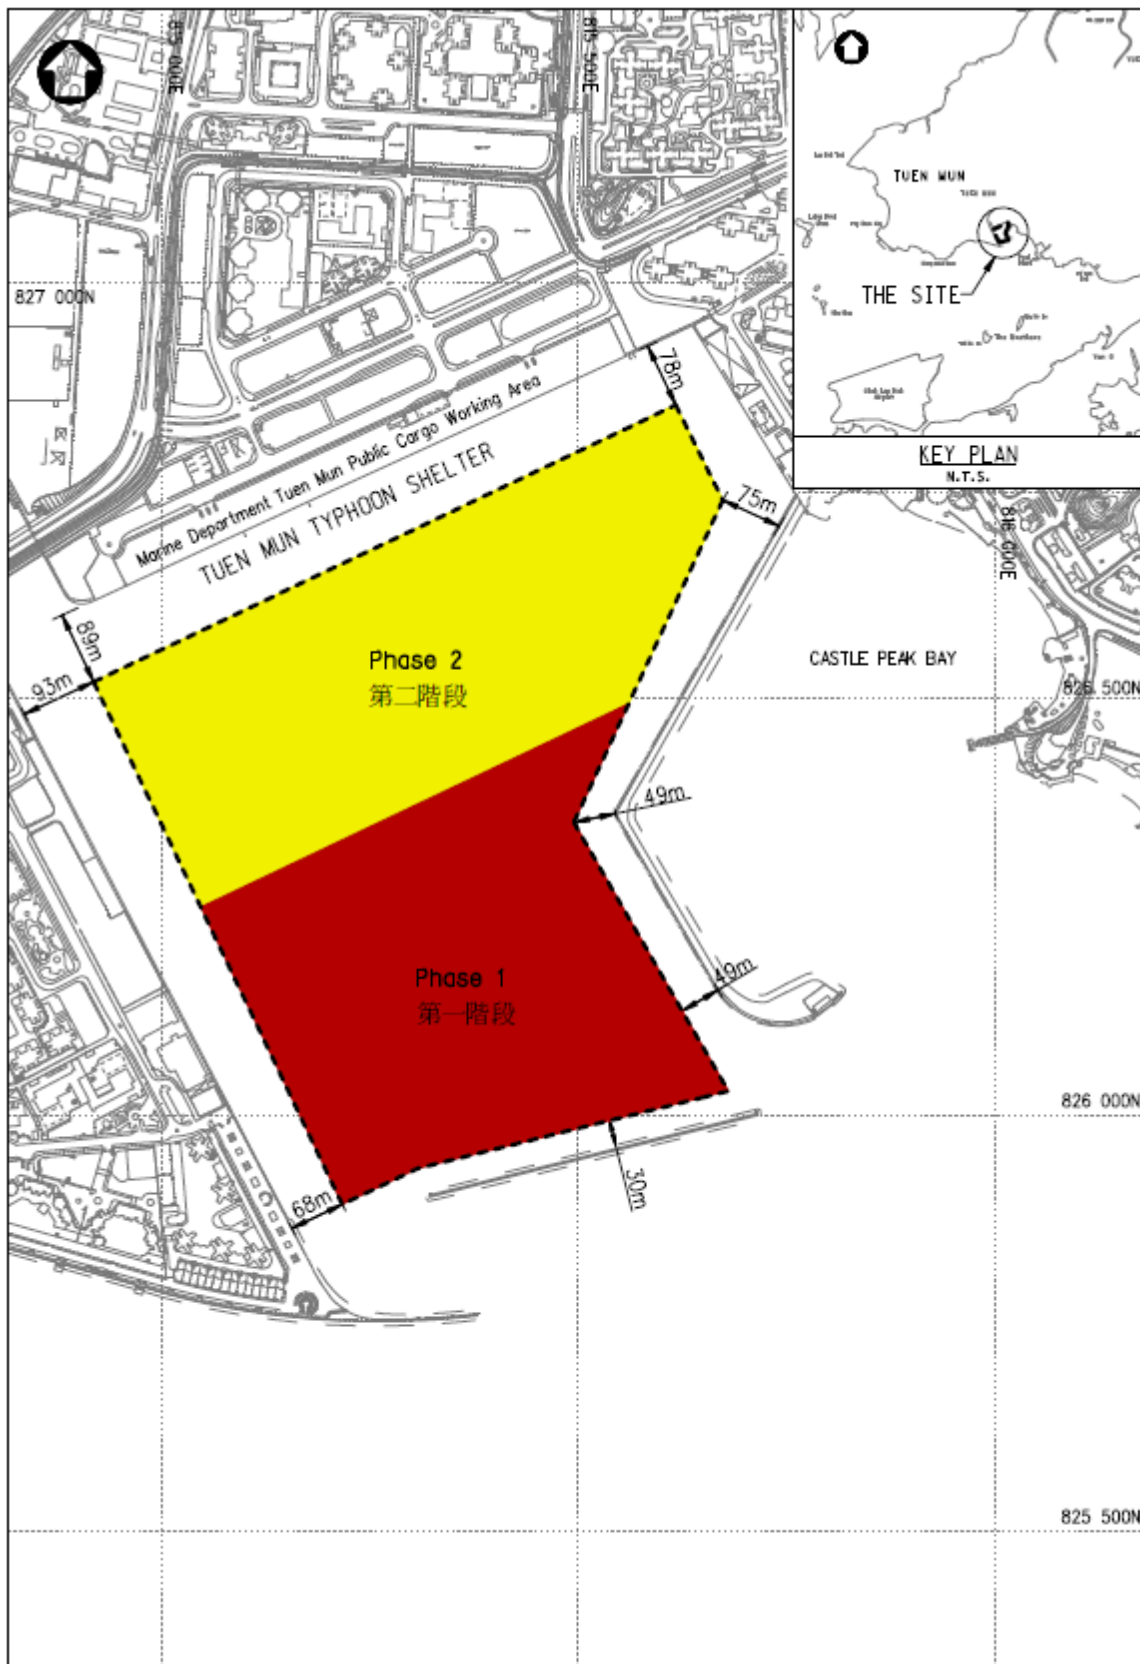

**Figure 1:** Location Plan of Tuen Mun Typhoon Shelter Dredging Works

水務署有關屯門區水管修復或敷設工程的進度匯報 (截至 2 月 28 日)

為改善屯門區內供水設施，水務署現正在區內進行的水管工程合約如下：

進行之水管修復或敷設工程及進度如下：

編號	合約編號	工程位置	長度 (米)	水管直徑 (毫米)	動工日期	完工日期	進度	備註
1	12/WSD/20	青賢街、河旁街、屯門鄉事會路	540	40 100	Q2/2022	Q2/2025	95%	鋪設水管進行中。
2	12/WSD/20	華發街	600	150 200	Q3/2023	Q2/2025	95%	鋪設水管進行中
3	3/WSD/21	湖山路至湖翠路	1440	200 250	Q3/2022	Q1/2025	90%	鋪設水管進行中。
4	3/WSD/21	龍門路	200	900	Q4/2023	Q1/2025	20%	鋪設水管進行中。
5	3/WSD/21	屯門鄉事會路 近屯興路	80	375	Q1/2024	Q2/2025	50%	鋪設水管進行中。
6	3/WSD/21	屯門鄉事會路 近友愛邨	150	375	Q4/2024	Q2/2025	5%	此路段已通過試路,工程將會隨即展開。
7	12/WSD/20	天后路	20	150	Q2/2022	Q1/2025	100%	鋪設水管完成。

計劃中的水管修復或敷設工程如下：

合約編號	工程位置	長度 (米)	水管直徑 (毫 米)	動工日期	完工日期	備註
10/WSD/24	屯門石排頭 路近建發街	195	50 100 150 250	Q4/2025	Q4/2027	現階段因遇到技術性問題，工程需要進行進一步研究後才能繼續展開。

水務署  
2025 年 2 月
