

**Tuen Mun District Council**  
**2024-2027 District Facilities and Works Committee**

**Progress Report on Other Government Departments' Works Projects (as at 30.4.2025)**

No.	Items	Government Departments	Progress Reports
A.	Drainage Services Department's Progress Report	Drainage Services Department	See <b>Annex I</b>
B.	Progress Report of Water Main Laying Works in Tuen Mun District by the Water Supplies Department	Water Supplies Department	See <b>Annex II</b> *

\* Only Chinese version is available

## Drainage Services Department's Progress Report

### I. Progress of Channel Desilting at Tuen Mun River Channel (as at 30.4.2025)

Location	Length (m)	Department	Actual Commencement Date (Anticipated Commencement Date)	Actual Completion Date (Anticipated Completion Date)	Progress/Remarks
Pui To Road to Tuen Ma Line Siu Hong Station	2400	DSD	01/2025	03/2025	Works completed
			04/2025	(06/2025)	Works in progress
			(07/2025)	(09/2025)	Works under planning
			(10/2025)	(12/2025)	Works under planning
Tuen Ma Line Tuen Mun Station to estuary	1800	CEDD	According to the bathymetric survey carried out in 2024 Q4, the riverbed level in the concerned river sections did not exceed the trigger level set by DSD. CEDD will continue to regularly carry out bathymetric survey and inspection to monitor the riverbed level. CEDD will carry out the dredging works if the riverbed level is found to affect the flood prevention capacity of Tuen Mun River.		

### II. Dredging Works at Wholesale Fish Market in Area 44 and Tuen Mun Typhoon Shelter

CEDD completed the dredging works for the Marine Department at Tuen Mun Typhoon Shelter Phase 1 and Phase 2 in end April 2020 and end April 2021 respectively. The locations are shown in **Figure 1**.


### III. Tuen Mun Village Sewerage

#### Contract No. DC/2020/07 – Village Sewerage in Northern Tuen Mun

The project includes the construction of one sewage pumping station at Fuk Hang Tsuen (Lower) and public sewerage systems in Siu Hang Tsuen, Po Tang Ha, Tsz Tin Tsuen, Fuk Hang Tsuen (Lower). The contract commenced in January 2021 and was substantially completed in December 2024.

**Drainage Services Department**

**April 2025**

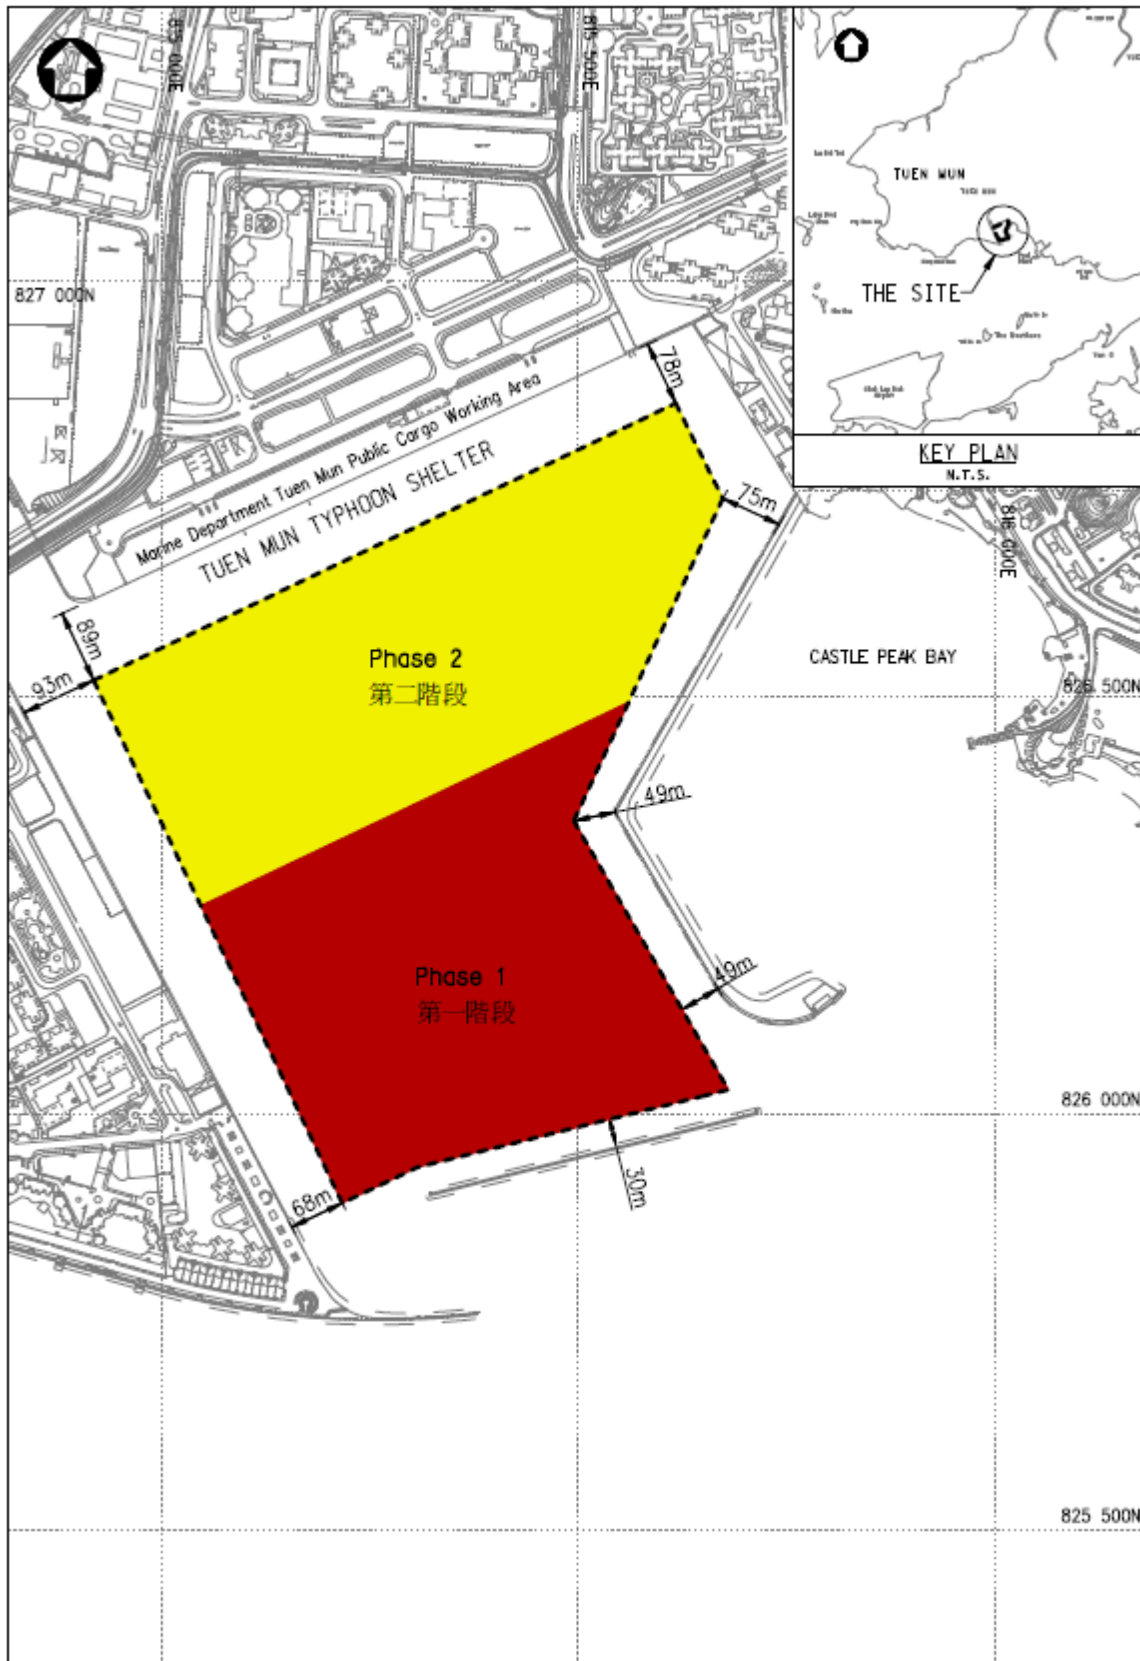

**Figure 1:** Location Plan of Tuen Mun Typhoon Shelter Dredging Works

水務署有關屯門區水管修復或敷設工程的進度匯報 (截至 4 月 30 日)

為改善屯門區內供水設施，水務署現正在區內進行的水管工程合約如下：

進行之水管修復或敷設工程及進度如下：

編號	合約編號	工程位置	長度 (米)	水管直徑 (毫米)	動工日期	完工日期	進度	備註
1	12/WSD/20 & 10/WSD/24	青賢街、河 旁街、屯門 鄉事會路	540	40 100	Q2/2022	Q4/2025	95%	鋪設水管完成，現 正分階段進行接 駁工程。
2	12/WSD/20	華發街	600	150 200	Q3/2023	Q2/2025	95%	鋪設水管完成，現 正分階段進行接 駁工程。
3	3/WSD/21	湖山路至湖 翠路	1440	200 250	Q3/2022	Q2/2025	95%	鋪設水管進行中。
4	3/WSD/21	龍門路	200	900	Q4/2023	Q2/2025	20%	鋪設水管進行中。
5	3/WSD/21	屯門鄉事會 路近屯興路	80	375	Q1/2024	Q2/2025	50%	鋪設水管進行中。
6	3/WSD/21	屯門鄉事會 路近友愛邨	150	375	Q4/2024	Q4/2025	5%	鋪設水管進行中。

計劃中的水管修復或敷設工程如下：

合約編號	工程位置	長度 (米)	水管直 徑 (毫 米)	動工日期	完工日期	備註
10/WSD/24	屯門石排頭 路近建發街	195	50 100 150 250	Q4/2025	Q4/2027	現階段因遇到技術 性問題，工程需要 進行進一步研究後 才能繼續展開。
10/WSD/24	天后路近天 后廟廣場	280	250	Q4/2025	Q4/2027	規劃中。

水務署

2025 年 4 月
